

RELIEF WELL #2
Development Driller II

DISCOVERER ENTERPRISE DRILL SHIP
Original MC 252 #1 Subsea Containment

RELIEF WELL #1
Development Driller III

RELIEF WELLS & SUBSEA CONTAINMENT

PROGRESS


- ▶ DDII - MC 252 #2
- ▶ Spudded well - May 16th
- ▶ Set 36" casing at 5,471' - May 16th
- ▶ Set 28" casing at 6,614' - May 21st
- ▶ Set 22" casing at 8,576' - May 24th
- ▶ Set 18" casing at 9,898' - June 20th

PROGRESS

- ▶ DDIII - MC 252 #3
- ▶ Spudded well - May 2nd
- ▶ Set 36" casing at 5,494' - May 2nd
- ▶ Set 28" casing at 6,730' - May 5th
- ▶ Set 22" casing at 8,762' - May 8th
- ▶ Set 18" casing at 9,945' - May 24th
- ▶ Set 16" casing at 12,057' - June 2nd
- ▶ Set 13 5/8" casing at 13,869' - June 9th
- ▶ Set 11 7/8" casing at 15,836' - June 19th

OVERVIEW

BP intends to drill two wells designed to intersect the original wellbore above the oil reservoir. This will allow heavy fluid to be pumped into the well which will stop the flow of oil from the reservoir. Cement will then be pumped down to permanently seal the well.

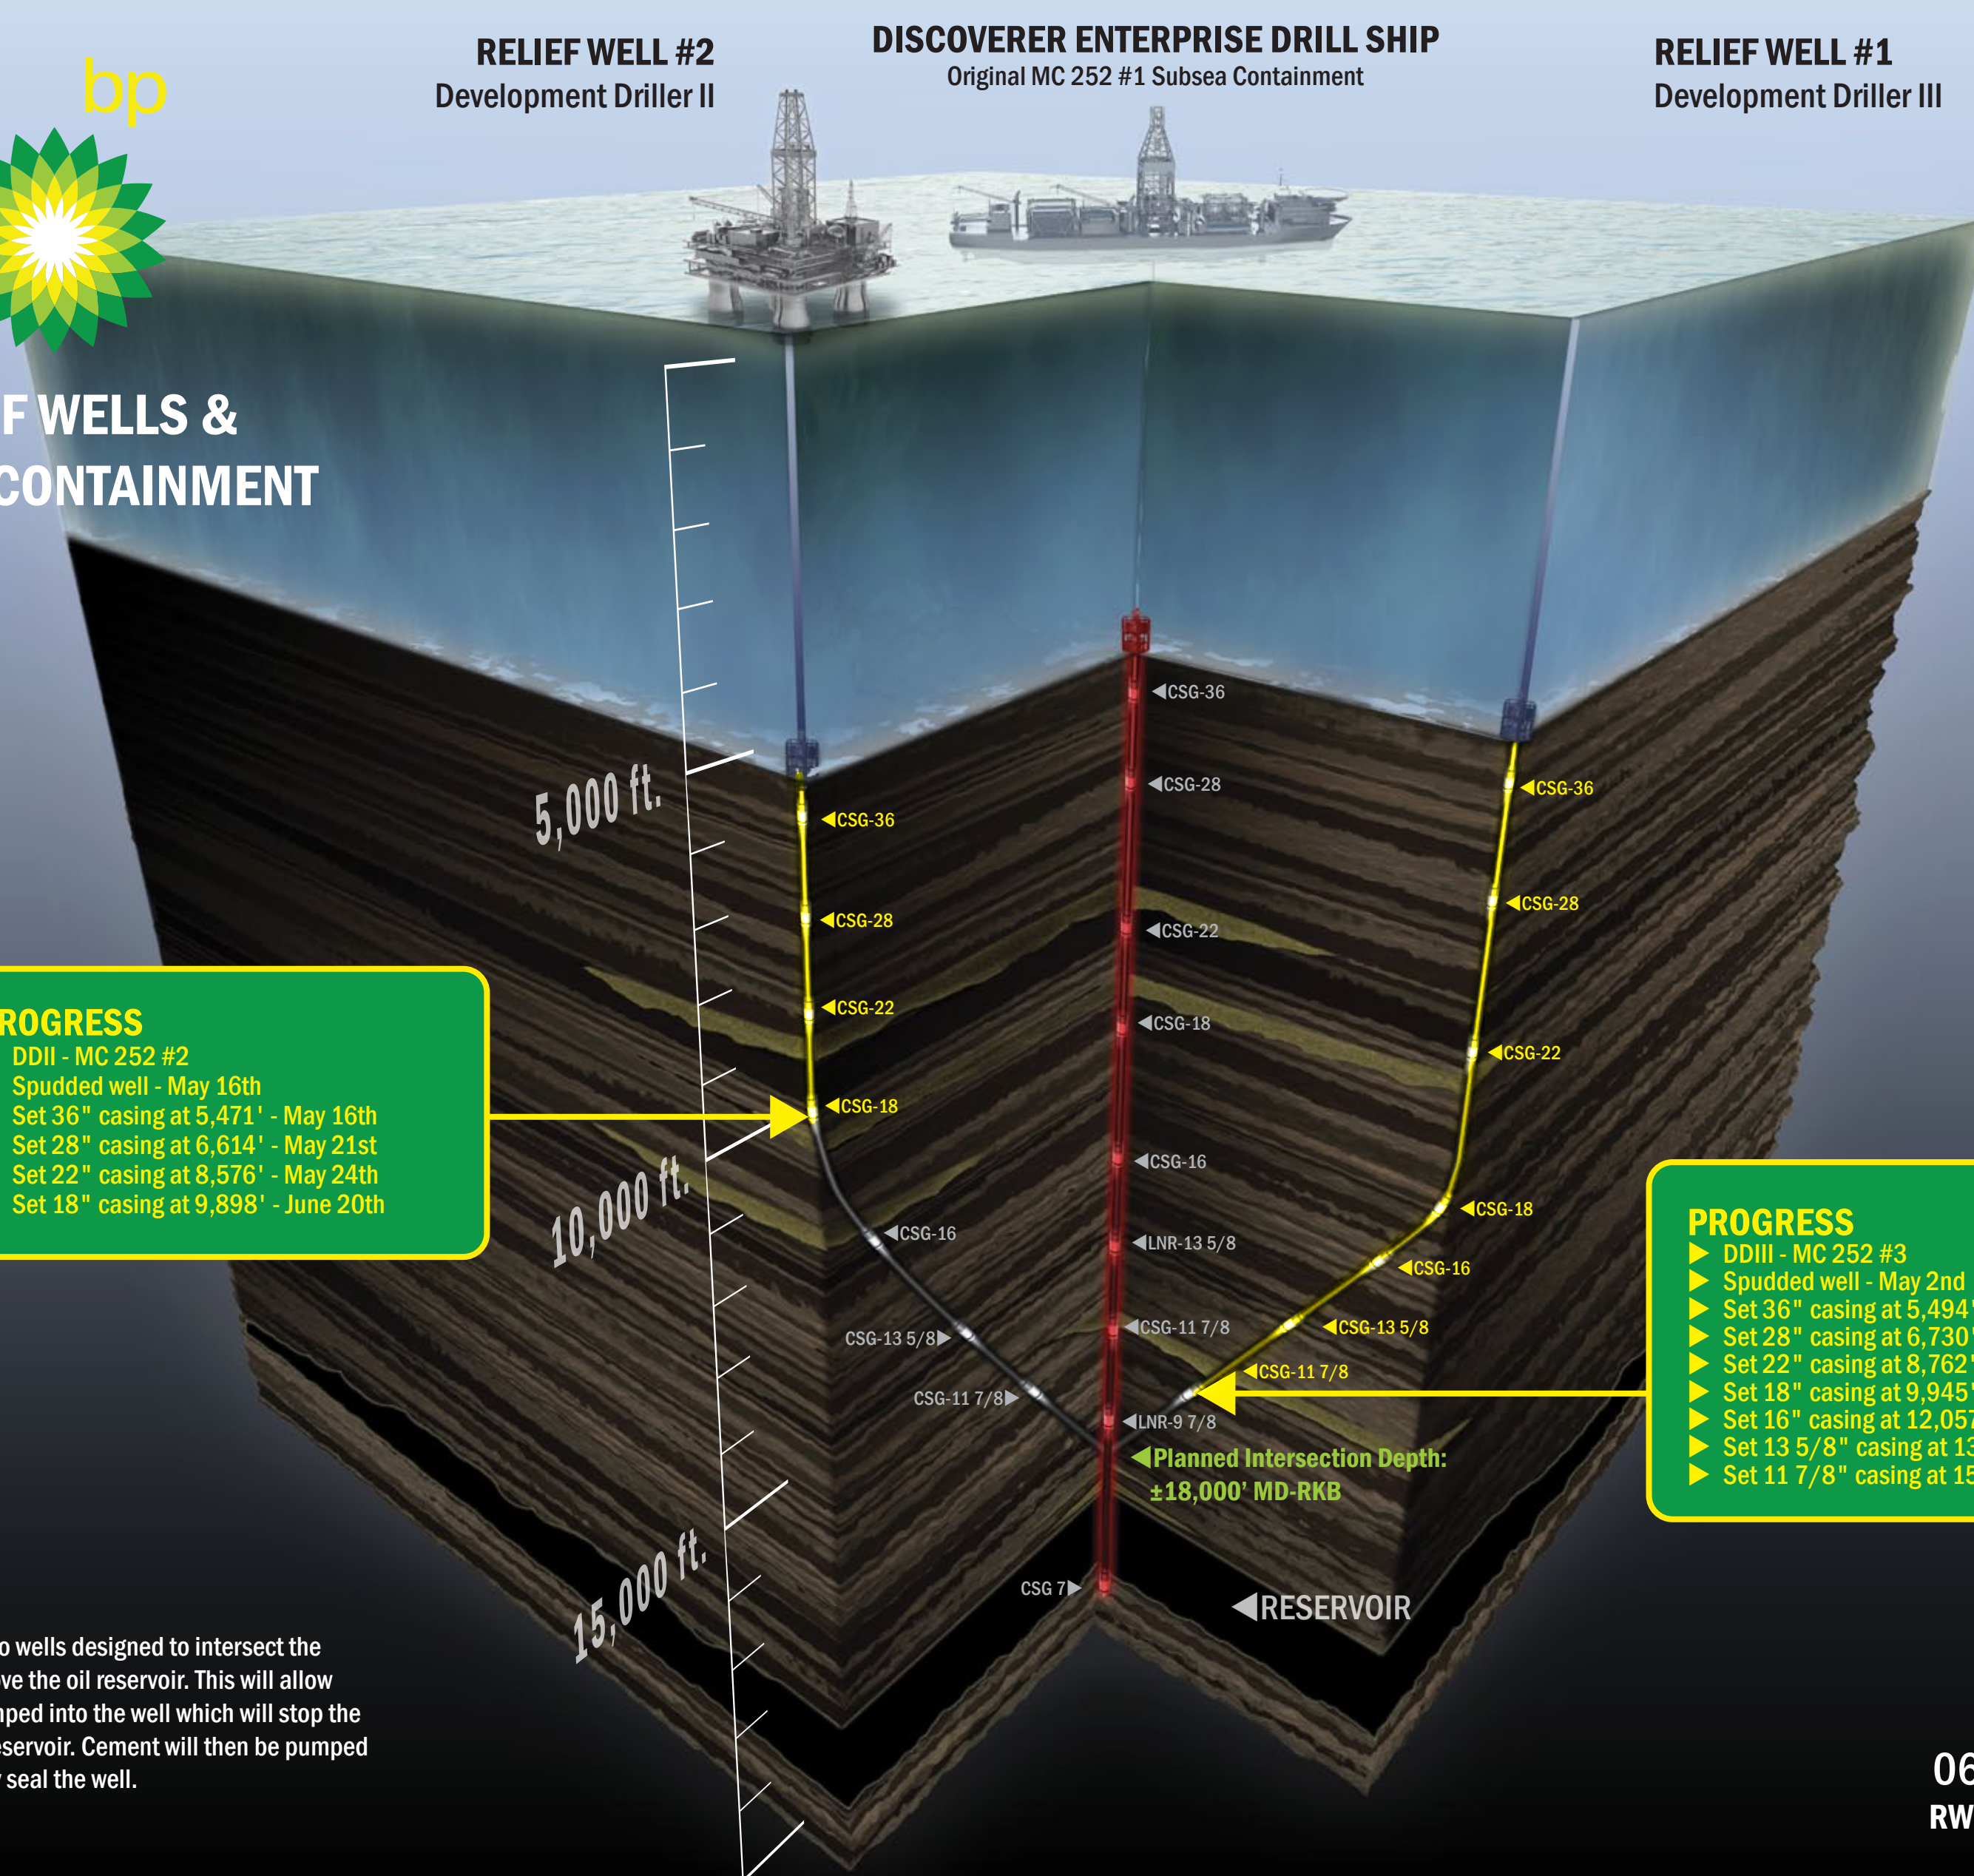

06/20/2010
RWD06202010V1
